



CONTACT DETAILS:

Darren Holmes, Site Manager 07855438063 Mon-Fri 8.30am-5pm
Darren.holmes@balfourbeatty.com
Tina Phillips, Liaison Officer 07854199719 Mon-Fri 8.30am-5pm
Tina.phillips@balfourbeatty.com

Project Details

The project involves the construction of a new 2 Storey classroom block including 7 classrooms, a resource room, associated WC's, circulation and plant rooms together with a new build extension to existing kitchen and main hall with new car parking and covered cycle store.

Works are progressing well.

Works carried out so far

Internal works progressing well with the exception of the window walls and bulkheads. Floor screed has been completed. 1st fix electrical completed to allow closing up and completion of plaster boarding. Fire stopping works ongoing to partitions. Plaster works commenced on 1st floor. Decorations to plant room have commenced to enable fit out works to start shortly.

What's coming up

- External cladding progression
- Roof abutment works
- Ground floor plaster works
- Stair-well plaster boarding and plaster works.
- Internal joinery

Progress Photographs



Ceiling boarding and access hatch works.




Plant room plastering works.



Bulkhead works.



Ground floor classroom

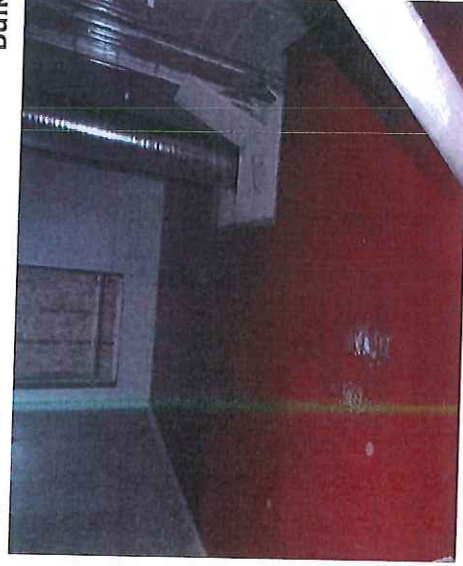

Plant room
